



Burton Way Median Green Street and Water Efficient Landscape Project Construction Update

Public Works Commission

December 14, 2023



Landscaping





Landscaping





Landscaping







Electrical Hot-Tie Oakhurst







Electrical Hot-Tie Rexford

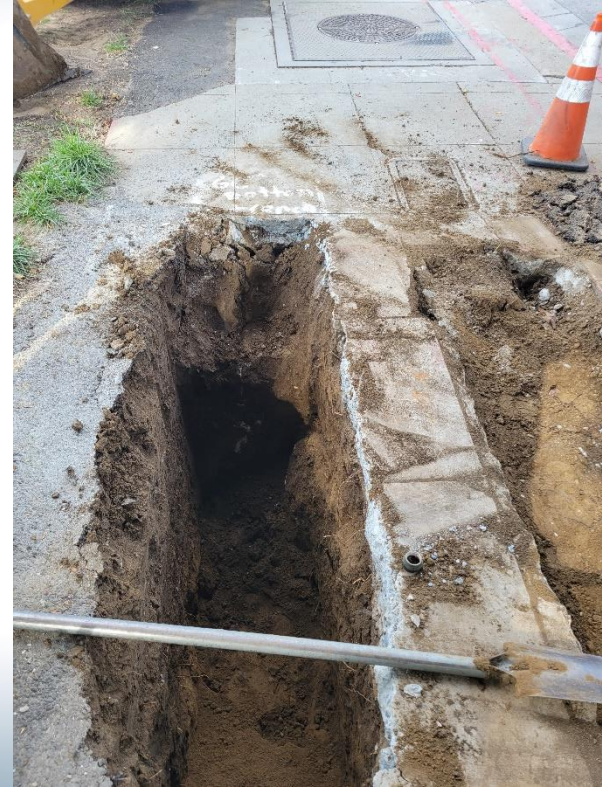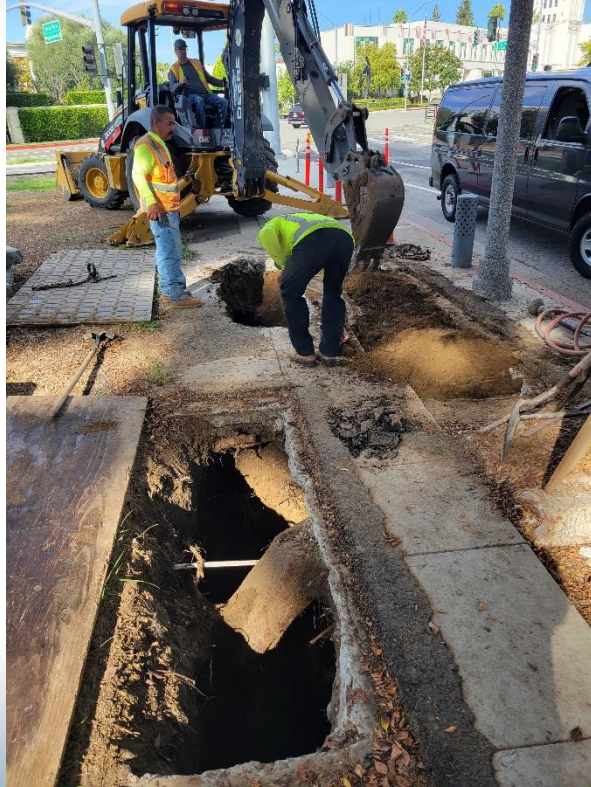



PLC Assembly

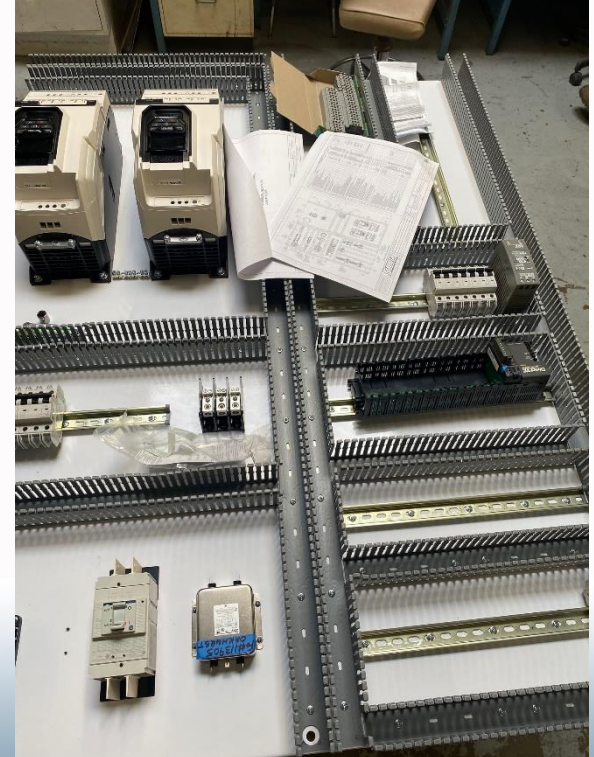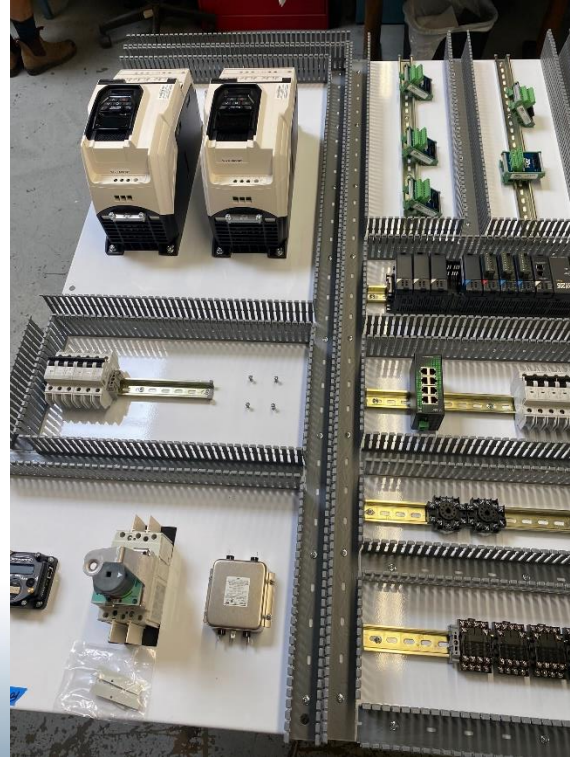



Project Overview

- Project Budget: \$13,376,592 (including design)
- Expended to date: \$12,616,523
- Construction Budget: \$11,992,500
 - Work Billed: \$11,319,023
 - \$7,164,615 Grant funding spent on construction
 - Percentage Work Complete: 94%
 - Estimated Completion Date: February 2024
