



La Brea LCW-1 and Sand Pit Sites Updates

Public Works Commission

May 12, 2022



LCW-1 Equipping



Pavement Prep Work



LCW-1 Equipping



Framing, Painting, Pavement




LCW-1 Equipping



Electrical Work



LCW-1 Equipping

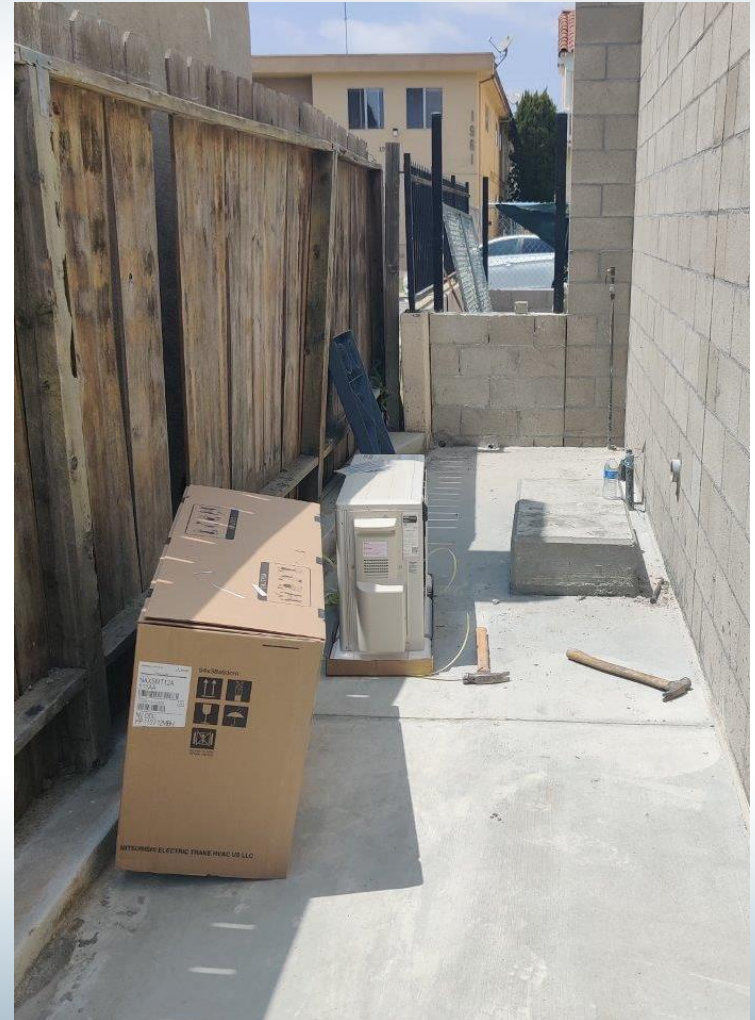

Electrical & HVAC



La Brea Subarea Overview

LCW NO. 1 – EQUIPPING

- Budget: \$2,900,000
- Work Billed: \$1,868,622
- Percent Work Complete: 70%

SAND PIT – Nested Monitoring Well

- Budget: \$884,276
- Work Billed: \$797,625
- Percent Work Completed: 100%



La Brea Subarea Development Project Timeline

Beverly Hills La Brea Subarea - La Cienega Well No. 1, Transmission Main, and Sand Pit Site Project Timeline May 2022

